




**BLOCKING PLAN**

Address: \_\_\_\_\_ Permit #: \_\_\_\_\_

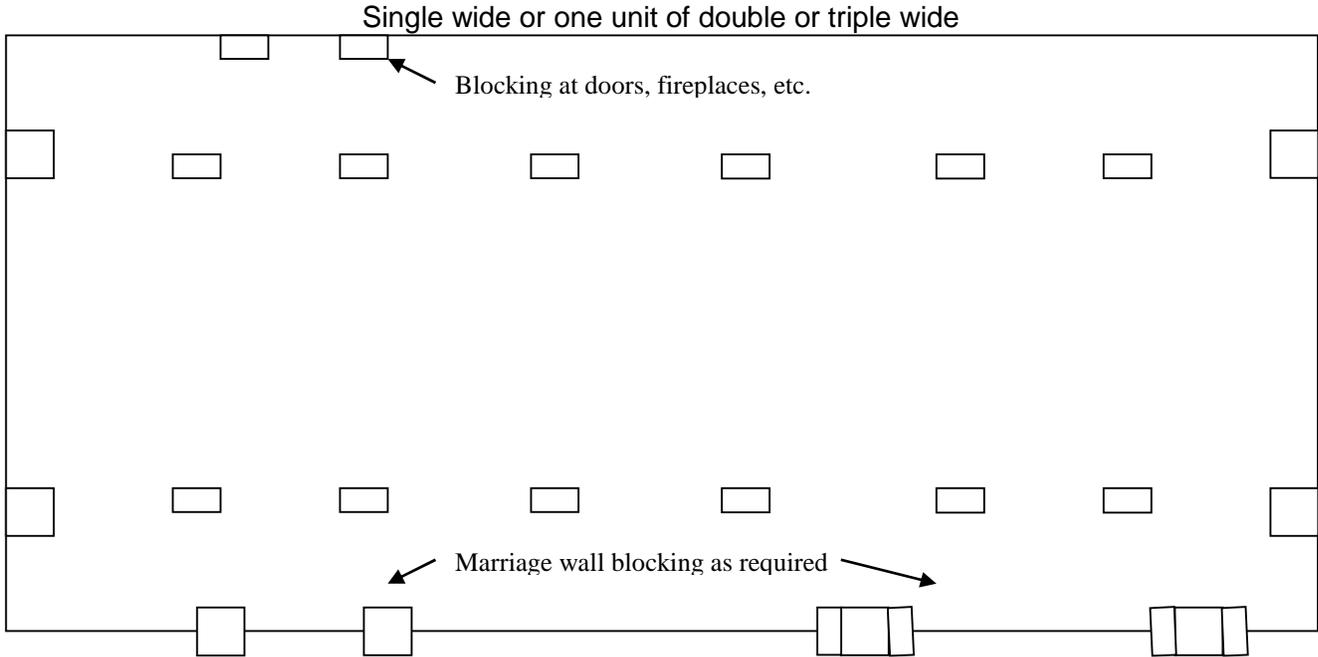

**Complete All Below:**

Year and Make _____	Single-Wide _____	Torque test for anchors:
Size of Home _____	Double-Wide _____	276in/lbs or more _____ (4ft anchors)
Tested Soil PSF _____	Additional Units _____	275in/lbs or less _____ (5ft anchors)
Footer (pad) size _____	Block Spacing _____	

Marriage Wall Case Opening Width \_\_\_\_\_ Roof Overhang (1.5", 6", 12" 24") \_\_\_\_\_

**IMPORTANT NOTES:**

- 1) End blocking required within one (1) foot of ends.
- 2) Above blocking typical - number varies with length.
- 3) Home must have a HUD label and must be approved for wind zone II or III.
- 4) Marriage walls to be adequately supported.
- 5) Straps not to exceed 5' 4" O.C. homes manufactured after 3/29/99.
- 6) After 5/29/99, longitudinal ties required (two (2) straps and anchors per end of beams).
- 7) Torque test value of less than 276 in/lbs requires 4000lb working load anchors (5ft).

The above information and testing are in accord with Rule 15C of the Department of Highway Safety and Motor Vehicles.

\_\_\_\_\_  
 (Signature of Contractor)

STATE OF FLORIDA  
 COUNTY OF BAY

Sworn to (or affirmed) and subscribed before me this \_\_\_\_\_ day of \_\_\_\_\_, 20\_\_\_\_,  
 by \_\_\_\_\_.

\_\_\_\_\_  
 (Signature of Notary Public - State of Florida)  
 (Notary Stamp or Seal)

Personally Known \_\_\_\_\_ OR Produced Identification \_\_\_\_\_

Type of Identification Produced \_\_\_\_\_
